



Introducing Starfish Construction

RE: Introducing Starfish Construction RE: Cladding Remediation Works – 16–18 Marshalsea Road, London, SE1 1HL

Dear Resident,

We are writing to inform you of the upcoming cladding remediation works, which form part of essential safety improvements across the development.

Starfish Construction have been appointed to carry out the removal and replacement of the existing render & stonework facade systems at **16–18 Marshalsea Road**, including works to the elevations facing **Disney Place, Disney Street** and **Redcross Way**. Our aim is to deliver a safer, more resilient, and fully compliant building envelope while keeping you informed and minimising disruption throughout the programme.

Project Timeline and Location

- **Welfare Setup** From **15 June 2026**, our team will be setting up the **welfare area** at the rear of the building on **Disney Street** to support ongoing works.
- **Scaffolding Installation:** Start 22/06/2026 (approx. 4 – 6 Weeks)
- **Duration:** 24 weeks
- **Working Hours:** Monday–Friday, 8am–5:00pm (*Workforce arrives at 7:30am; noisy works will not begin before 8:00am*)
- **Occasional Saturday working** may be required
Location: 16–18 Marshalsea Road, London, SE1 1HL

Scope of Works

- **Removal of existing facade materials** including render, insulation, and any non-compliant components.
- **Installation of a new compliant external wall system**, including non-combustible insulation and upgraded fire-stopping.
- **Localised structural repairs** where required following strip-out.
- **Installation of upgraded stone cills and head extensions** to improve performance and appearance.
- **Full-depth cavity insulation** to enhance fire safety and energy efficiency.
- **Dust and noise control measures** to minimise disruption.
- **Cleaning of external facades** on completion.
- **Safe access always maintained** for residents and visitors.
- **Regular liaison and updates** throughout the project.

These works are essential to ensure long-term safety, compliance, and building performance.

Expected Disruptions

- **Increased noise** from drilling and facade removal
- **Temporary footpath diversions** around Marshalsea Road, Disney Place, and Redcross Way
- **Delivery vehicles** entering/exiting the site
- **Dust control measures**, though minor disturbances may still occur
- **Reduced parking or loading access** where required for safety
- **All works** will comply with strict health, safety, and environmental regulations.

Scaffolding & Access

To safely access all elevations, scaffolding will be erected around the building.

Key features include:

- **Full perimeter scaffolding**
- **Goods hoist** for material movement

Walkway tunnels at:

- Marshalsea Road main entrance
- Disney Place
- Redcross Way

If you have any questions or would like more information, please feel free to get in touch with Courtney Greatorex your resident liaison officer at cgreatorex@starfishltd.com or 07939894015 — she'll be more than happy to help!



Weekly Progress Update Week Ending: 17th July 2026

The project has continued to progress well this week as we move through the early stages of the programme. Despite periods of poor weather, key access and setup works have advanced across both elevations. Thank you for your continued cooperation — your support helps us maintain a safe, efficient and well-coordinated site.

Progress Highlights This Week – Week Ending 17/07/2026

Site Progress

- **Phase 1 scaffold** has now been fully netted and formally handed over for use.
- **Phase 2 scaffold** erection has commenced and is progressing well.
- A new **hoist** and Haki stair have been installed to support safe movement of operatives and materials.
- **Temporary power** installation to Phase 1 is now complete.
- Protection to windows has begun in preparation for upcoming **render removal** works.
- Dilapidation surveys are almost complete — **Apartment 1 is the only outstanding property**.
- To reduce noise levels on site, the welfare facilities have now been hard-wired, removing the need for a generator.

What Residents Can Expect Next Week – Week Commencing 20th July 2026

Scaffolding & Access

- scaffold erection will continue to Phase 2 along the Marshalsea Road elevation.
- Protection works will continue ahead of render removal.
- Render removal will begin in selected areas once protection is fully installed.

Internal Dilapidation Surveys

- Apartment 2 remains outstanding. The Resident Liaison Officer will be in touch to arrange access.
- All surveys must be completed promptly to ensure compliance and protect residents' homes during the works.
- Resident Liaison Officer: **Courtney Greateorex** M: **07939 894015** E: CGreateorex@starfishltd.com
-

Message From the Starfish Team

Thank you for your continued cooperation across site. Whether it's adjusting routines, following temporary diversions, or taking extra care around active work areas, your support makes a real difference. It helps us maintain a safe, well-coordinated and efficient programme as we move through each stage of the works.

With warmer weather expected over the coming days, please take extra care to keep your home ventilated where possible and stay cool during hotter periods, especially while balcony access remains restricted.

We truly appreciate your patience and understanding and remain committed to keeping you informed every step of the way.

If you have any questions or would like more information, please feel free to get in touch with Courtney Greateorex your resident liaison officer at cgreateorex@starfishltd.com or 07939894015 — she'll be more than happy to help!




Photographic Evidence

Phase 1 Marshalsea Road Elevation



Phase 1 Disney Place

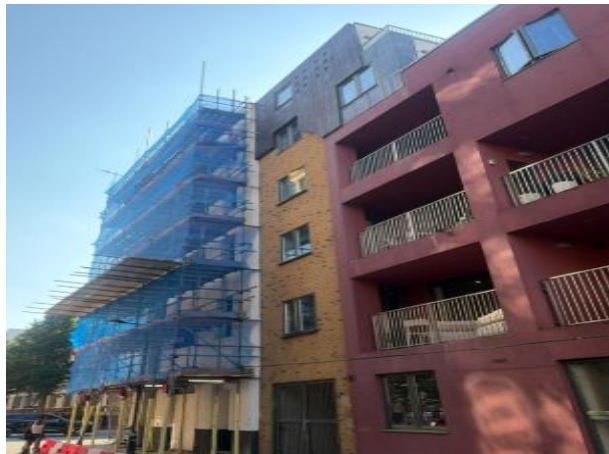

Welfare Setup & Compound Establishment – Completed

Location: The welfare area is positioned at the rear of the building on Disney Street, as outlined in the introduction letter.



If you have any questions or would like more information, please feel free to get in touch with Courtney Greatorex your resident liaison officer at cgreatorex@starfishltd.com or 07939894015 — she'll be more than happy to help!



The Information Above outlines the initial stages of the remediation works to Borough Place. For more detailed information on the project including specific start dates and durations relevant to your apartment.

please contact me at **CGreatorex@starfishltd.com** or by telephone on **07939 894015**, providing the following information:

- Name
- Email address
- Telephone number
- Occupancy type (Leaseholder/Renter)

We greatly appreciate your cooperation and patience while these important safety works are carried out. Our team is committed to minimising disruption and keeping you fully informed throughout the project.

Yours Sincerely

Courtney Greatorex
Resident Liaison Officer
T: 07939 894015
E: CGreatorex@starfishltd.com

Visit Our Dedicated Residents and Stakeholders Hub

Starfish Construction is delighted to bring you this dedicated online resource designed exclusively for residents and stakeholders. We aim to provide you with valuable information about the project, the work to be carried out, schedules, introduce the project team, and, most importantly, ensure your safety and well-being throughout the construction process.

Two areas serve as your primary source of information and updates throughout the project – **The Residents and Stakeholders Hub** and the **Updates and Announcements section**.

You can sign up to receive any project updates and announcements by visiting the website address below or by scanning the QR code with your compatible device.

<https://www.starfishconstruction.com/borough-place-hub>



We greatly appreciate your cooperation and patience while these important safety works are carried out. Our team is committed to minimising disruption and keeping you fully informed throughout the project.

If you have any questions or would like more information, please feel free to get in touch with Courtney Greatorex your resident liaison officer at cgreatorex@starfishltd.com or 07939894015 — she'll be more than happy to help!
