

Statement from Courtney Greatorex - Resident Liaison Officer at Bedford and Leicester Courts - Moor Lane & Cregg Lane, Preston

We are pleased to inform you that Starfish Construction has been appointed by **Miller Homes** to carry out the works at **Bedford and Leicester Courts**.

Please find below the latest updates regarding the reinstatement works and onsite activities scheduled for the week commencing **Monday 16th February 2026**.



News & Updates

Weekly Site Progress Update

The team has continued to make strong, coordinated progress across all towers this week, with several elevations advancing through key stages of the façade removal and rebuild process. Works are moving steadily and safely, and your continued patience is helping us maintain this positive momentum on site.

Upcoming Works Week Commence 16.02.2026 Looking ahead into the week, the team will be progressing with the following activities:

- **Elevation C – Towers 1, 2 & 3**

Similar progress has been achieved on Elevation C, where cladding and frame removal is now complete. Y-wall and silicone works have been installed, along with EPDM, Obex membrane, C-sections, brackets, and front rails. Steel sleeves are also **50% complete** on this elevation.

- **Elevation D – Towers 1, 2, 3 & 4**

Elevation D has seen significant activity, with cladding and frame removal completed across all four towers. The team has installed Y-wall and silicone, EPDM, Obex membrane, C-sections, brackets, and front rails. Steel sleeve installation is progressing well and currently sits at **50%**.

- **Elevation A1 & A2**

Cladding and frame removal has been completed on Elevations A1 and A2. Y-wall and silicone installation is now in place, along with EPDM, Obex membrane, and C-sections, preparing these areas for the next stages of the façade build-up.


News & Updates



Our Welfare unit is located on the front entrance to the car park area between Bedford and Leicester Court

News & Updates

Due to the cut-through patch currently being closed, please follow the directions shown on the diagram to access the main road,

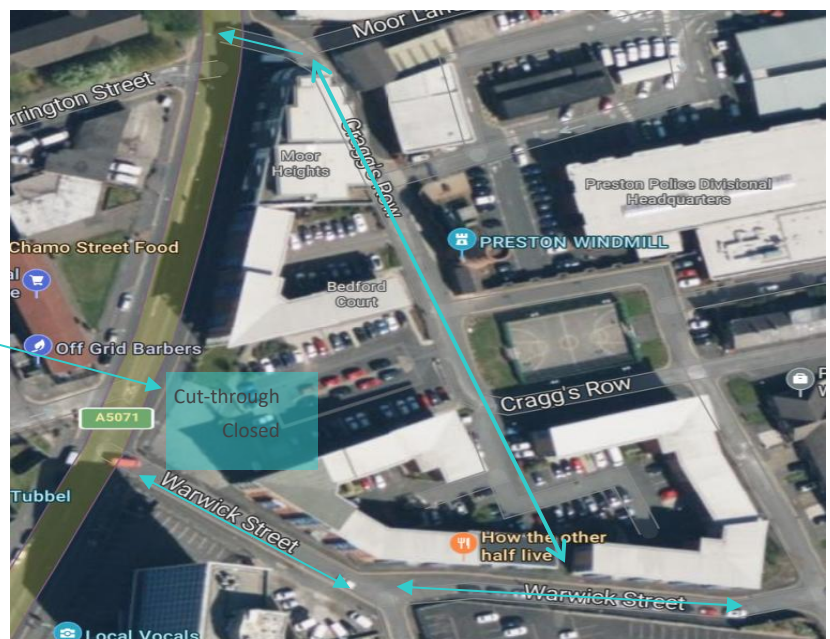



Contact information



Resident Liaison Officer

Name: Courtney Greatorex

Telephone: 07939 894015

Email: CGreatorex@starfishltd.com

Working hours: 8am-5:00pm



Site Manager

Name: Daniel Horwood

Telephone: 07940 022295

Email: dhorwood@starfishltd.com

Working hours: 8am-5:00pm
