



Statement from Amy Butzki - Resident Liaison Officer at St George's

Dear Residents and Leaseholders,

Welcome to the latest news and updates for St George's. Please find below the latest updates regarding the reinstatement works and onsite activities scheduled for the week ending **Friday, 20th February 2026**

News and Updates

Health & Safety

- No H&S issues to discuss.

Design

- Design complete.

Procurement

- EPDM & Breather membrane has been delivered.
- Render material has been delivered.
- Terracotta bracket & rails have been delivered,
- Insulation for terracotta area has been delivered.
- Cavity Barrier order has been placed & will be delivered to suit programme.

Production

- Starfish Project Manager has been onsite on 16.02.2026 & 17.02.2026 to prepare for labour to return to site on 18.02.2026
- Labour will commenced loading out of materials on the 18th & 19th February 2026
- Labour will commenced installation of new terracotta brackets on 19.02.2026
- Final preparation work to the render area on Phase 1 to allow the render insulation to commence from 23.02.2026








Resident Liaison Matters

- The next resident hub update will be 20.02.2026

Planning and Programming - W/C 23.02.026

- Continue installation of terracotta support system to Phase 1
- Commence install of Phase 1 render
- Continue load out material where required

Photographic Evidence

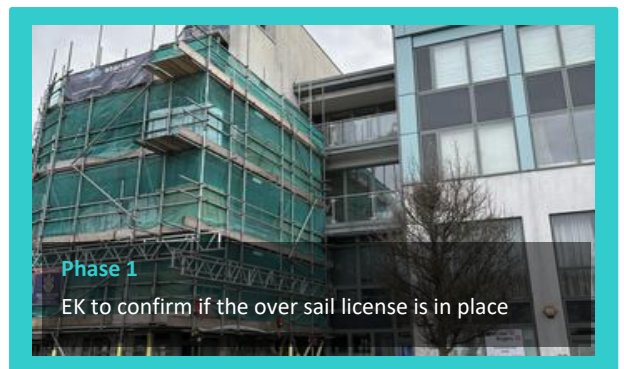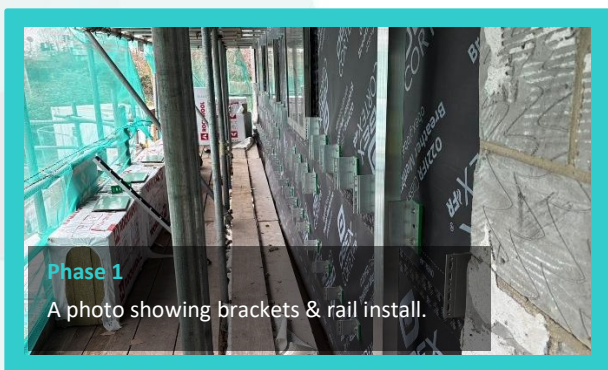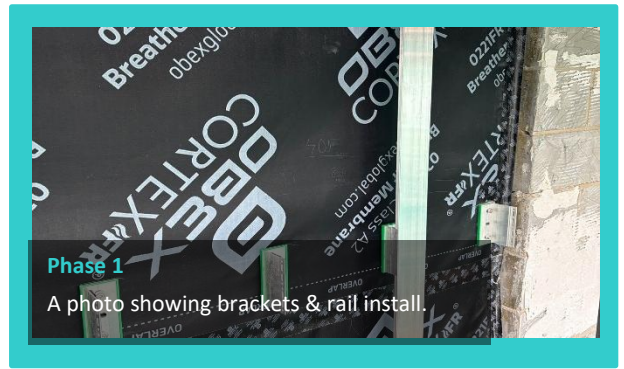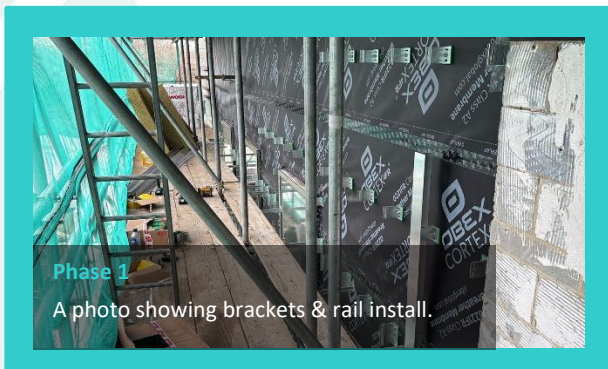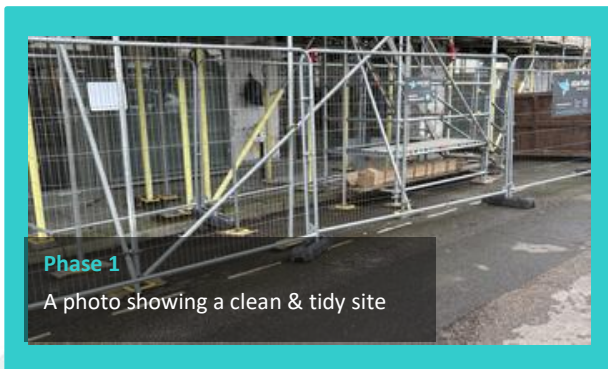



As part of our commitment to keeping you informed, please find below the latest update for **St George's**. These weekly reports will continue to provide regular updates on site activities, planned works, and any relevant notices.

If you have any questions or concerns regarding the ongoing works, please don't hesitate to contact your Resident Liaison Officer, **Amy Butzki** using the details provided below. Your continued cooperation and support are greatly appreciated as we work to deliver these improvements safely and efficiently.

