

Statement from Amy Butzki - Resident Liaison Officer at Turney's Court

Dear Residents and Leaseholders,

Welcome to the latest news and updates for Turney's Court. Please find below the latest updates regarding the reinstatement works and onsite activities scheduled for the week ending **Friday, 24th October 2025**. This section will provide regular progress reports, keeping you informed of the works taking place across all blocks, as well as any important notices that may affect residents during the construction period. Our aim is to ensure transparency, maintain open communication, and keep everyone updated on the ongoing improvements to the building.

News and Updates

Health & Safety

All weekly site paperwork has been completed and filed.

Design

- All design works are 90% complete.

Procurement

- Phase 1 & 2 materials are onsite.
- Phase 3 materials will commence delivery over the next 2 weeks.

Production

- Phase 1 All brackets/rails/insulation & fire barrier works are complete with cladding finish install commencing.
- Phase 2 All brackets/rails/insulation & fire barrier works are 50% complete.
- Phase 3 All existing cladding has been removed

Our Commitment

As part of our commitment to keeping you informed, please find below the latest update for Turney's Court - These weekly reports will continue to provide regular updates on site activities, planned works, and any relevant notices.

Planned Works for W/C 27.10.25


- Continue with cladding panel install on Phase 1.
- Continue with cladding backing structure works on Phase 2.

Photographic Evidence




Cedar Panel Installation

The installation phase for the panels has officially begun, marking visible progress on site. Currently, around 5% of the total panel installation has been completed, with works continuing steadily.

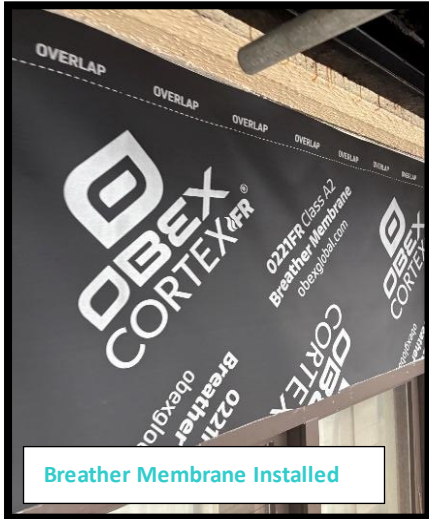

Breather Membrane Installed

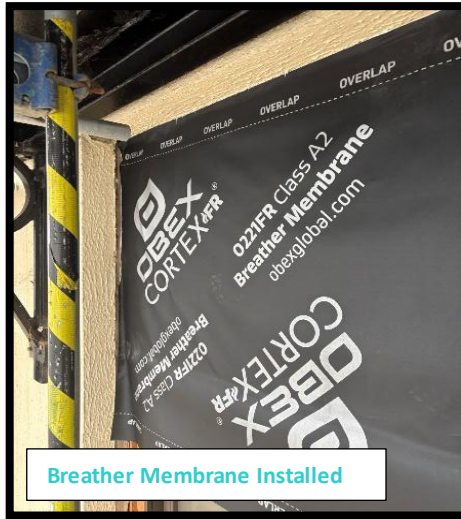

Breather Membrane Installed



EPDM, insulation & metal stud board

Rockwool Installed



If you have any questions or concerns regarding the ongoing works, please don't hesitate to contact your Resident Liaison Officer, **Amy Butzki**, using the details provided below. Your continued cooperation and support are greatly appreciated as we work to deliver these improvements safely and efficiently.

Contact Information



Resident Liaison Officer

Name: Amy Butzki
Telephone: 07539011441
Email: abutzki@starfishltd.com
Working hours: 9am-4:30pm



Site Manager

Name: Andrew Brown
Telephone: 07811396473
Email: abrown@starfishconstruction.com
Working hours: 8am-5:00pm
