

Statement from Courtney Greatorex - Resident Liaison Officer at Vincent House, Woodlands Road, Darlington DL3 7PN



Dear Residents and Leaseholders,

We are pleased to inform you that **Starfish Construction** has been appointed by **The Letting Group** and **Thomasons**, to carry out the works at **Vincent House**. Please see below the latest updates regarding the Cladding Remediation works and onsite activities. Scheduled to begin the week commencing **Monday 13th July 2026**

We will continue to keep you updated each week as the project progresses. Should you have any questions about the works, please do not hesitate to contact me directly.

Project Timeline and Location

- **Start Date:** Monday 13th July 2026
- **Week 1:** Installation of welfare, compound, scaffold and removal of all existing cladding panels and sub-structure
- **Week 2:** Installation of the new cladding system begins
- **Duration:** Approximately 5 Weeks
- **Working Hours:** Monday to Friday, 7:30 AM – 5:00 PM (*Please note the workforce will be arriving for 7:30 but no works to start till 8:00 AM, plus occasional Saturday work may be required*)
- **Location:** Vincent house, 2 Darlington, Durham, County DL3 7PN

Scope Of Works - Vincent House

The cladding remediation works will include:

- Removal of the existing cladding panels and sub-structure
- Installation of a new compliant sub-structure
- Installation of new fire barriers
- Installation of new aluminium cladding panels
- All works will be carried out from scaffold access
- These works are essential to ensure the building meets current fire safety and compliance standards.

Expected Disruptions

As a resident, you may notice the following during the course of the works:

- **Increased noise** from machinery, drilling, and removal of external facade materials
- **Delivery vehicles** entering and exiting the site during working hours
- **Dust and debris control** measures in place, though minor disturbances may still occur
- **Temporary adjustments** to access routes around the building
- **Reduced parking availability** in certain areas to allow safe working zones and material storage
- **All works** will be carried out in line with strict health, safety, and environmental regulations.

Residents Works Update - Week Ending 17.07.2026

The project has continued to progress well this week, with key early-stage works advancing safely and efficiently across site. Thank you for your continued cooperation — your support helps us maintain a well-coordinated and productive programme.

Progress Highlights – Week Ending 17.07.2026

Site Progress

- All works remain on programme, and full site possession has now taken place.
- **Scaffolding installation** was completed on **14 July 2026**, providing safe access for upcoming facade works.
- **Existing cladding removal** is now 98% complete, with only minor sections remaining.
- **Sub-structure setting out** has commenced in preparation for the new facade system.
- The welfare area has been successfully set up and is fully operational, supporting safe and efficient site activity.
- All enabling works have progressed smoothly, with teams working safely and effectively throughout the week.

What Residents Can Expect Next Week – Week Commencing 20.07.2026

Upcoming Works

- Installation of the new sub-structure will commence across the elevation, forming the next major phase of the facade reinstatement.
- Remaining cladding removal will be completed.
- Teams will continue progressing access and setup works to support the next stages of the programme.

Message From the Starfish Team

Thank you all once again for your continued cooperation across site. Your support — whether adjusting routines, following temporary diversions, or taking extra care around active work areas — makes a significant difference and helps us maintain a safe, efficient and well-coordinated programme.

We truly appreciate your patience and understanding as we move through these early stages of the works and remain committed to keeping you informed every step of the way.

PHOTOGRAPHIC EVIDENCE



Welfare & Compound

Picture showing welfare area set up.



Scaffold

Picture showing scaffolding to front elevation.

Visit Our Dedicated Residents and Stakeholders Hub

We want to make it easy for you to stay informed about the works in your compound. Scan the QR code or visit the link below to access your Residents & Stakeholders Hub.

Every week, we'll update you with:

- Works completed
- Upcoming activities for the week ahead
- Key information to help you plan around the works

Two areas serve as your primary source of information and updates throughout the project – **The Residents and Stakeholders Hub** and the **Updates and Announcements** section.


You can sign up to receive any project updates and announcements by visiting the website address below or by scanning the QR code with your compatible device.

<https://www.starfishconstruction.com/vincent-house-hub>

Connect to the Hub



Contact information

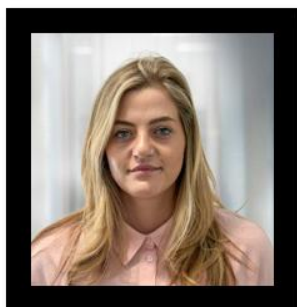

Resident Liaison Officer

Name: Courtney Greateorex

Telephone: 07939894015

Email: CGreateorex@starfishltd.com

Working hours: 9am-4:30pm



Site Manager

Name: Matthew Critchell



starfish
construction group

Weekly Progress Update

We look forward to meeting you and working together to ensure a smooth and positive experience throughout the duration of the project. If you have any questions in advance, please feel free to contact Courtney Greatorex, your Resident Liaison Officer.
