



Statement from Kevin Dickson - Resident Liaison Officer at Buchanan View Student Roost

Dear Residents and Leaseholders,

Welcome to the latest news and update for Buchanan View student roost. Please find below the latest updates regarding the works and onsite activities.

Scheduled for week commencing **Monday the 31st of August 2026**. This section will provide regular reports, keeping you informed of the works taken place across the blocks, as well as any important notices that may affect residents during the construction period. Our aim is to ensure transparency, maintain open communication, and keep everyone updated on the ongoing improvements to the building.

News and Update

Week commencing 31/08/2026

Important information.

The site will be open on Saturday the 29th of August from 9am until 4pm.

BLOCK 33

Phase 8 brickwork removal will start this week. These works will be noisy at certain times of the day.

Phase 5, 6, 7 and 8 Render works will continue this week.

Cladders will be working on phase 5, 6, 7 and 8 installing the new y wall, cavity barriers and new insulation.

BLOCK 35

Phase 1 and 2 render works to continue this week.

Phase 2 and 3 rain screen cladding will be completed this week.

Phase 4 new insulation and cavity barriers to be installed this week.

Phase 4 brickwork will continue this week

Phase 1 brickwork including high level will be complete this week

Phase 2 scaffolding will be removed this week after an inspection has taken place.




Should you have any questions about the works, please don't hesitate to contact Kevin Dickson- Resident Liaison Officer via email on kdickson@starfishltd.com or via telephone on **07496425229**



Block 35

Phase 1 (Purple) Phase 2 (L Blue) Phase 3 (Yellow) Phase 4 (D Blue)

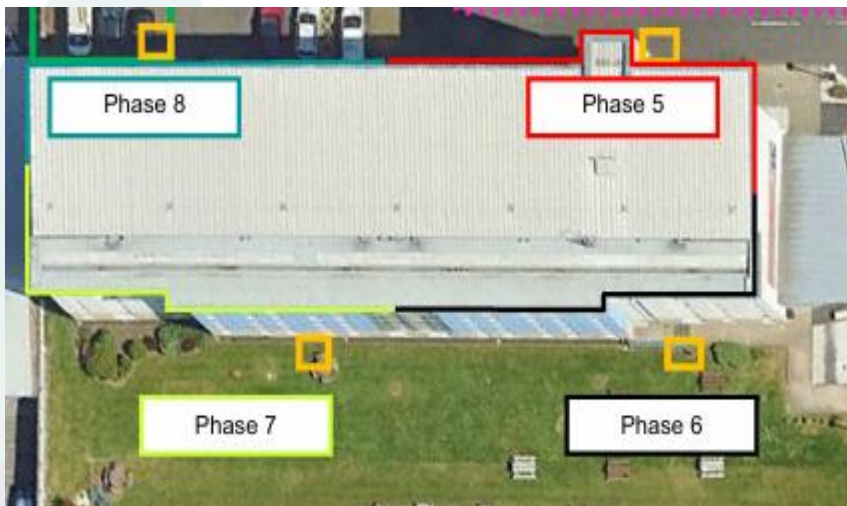

Block 33

Phase 5 (Red) Phase 6 (Black) Phase 7 (Green) Phase 8 (Blue)



Should you have any questions about the works, please don't hesitate to contact Kevin Dickson- Resident Liaison Officer via email on kdickson@starfishltd.com or via telephone on 07496425229

Scope of works

Façade Remediation including:

Site set up [including welfare area]
Install Barriers and fencing
Install scaffold access and working platforms
Install access hoists
Removal and replacement of brickwork and render
Removal and replacement of cladding
Installing Cavity barriers and non-combustible materials
Demobilize site

Project timeline and location

Start date: 06/10/2025

Duration: 57 weeks

Working hours: Monday to Thursday, 8.00AM - 5.00PM - 4PM Friday

Location: Buchanan View (blocks 33-35)

Expected Disruptions

As a resident you may notice the following during the works:

Increased Noise from machinery, drilling, and the removal of external façade materials

Temporary road or footpath closures around or near the building

Delivery vehicles entering and exiting the site during working hours

Dust and debris control measures are in place, though minor air disturbances may still occur occasionally

Reduced parking near the site compound to allow safe site access and material storage.

We will continue to keep you updated each week as the project progresses.

Should you have any questions about the works, please do not hesitate to contact Kevin Dickson.



Should you have any questions about the works, please don't hesitate to contact Kevin Dickson- Resident Liaison Officer via email on kdickson@starfishltd.com or via telephone on [07496425229](tel:07496425229)
