


Statement from Courtney Greatorex - Resident Liaison Officer at Bedford and Leicester Courts - Moor Lane & Cregg Lane, Preston

We are pleased to inform you that Starfish Construction has been appointed by **Miller Homes** to carry out the works at **Bedford and Leicester Courts**.

Please find below the latest updates regarding the reinstatement works and onsite activities scheduled for the week commencing **Monday 16th March 2026**.

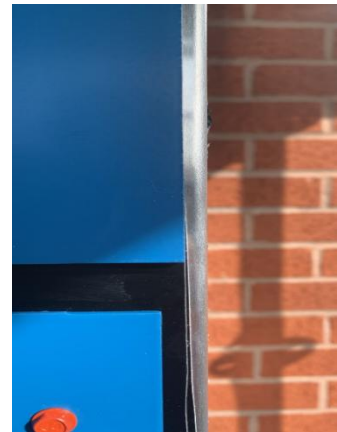

News & Updates

Weekly Site Progress Update

The team will continue to make steady progress across Elevation D next week, with a strong focus on completing key stages of the facade build-up. Coordination between teams remains excellent, helping us maintain momentum as we move toward panel installation.

Upcoming Works – Week Commencing Monday 16th March 2026

Elevation D – Towers 1, 2, 3 & 4

Primary Focus: The main priority for the coming week is the continuation of **fire barrier and insulation installation** across Elevations D1, D2, D3 and D4. These works are progressing well and will form the foundation for the next major phase of the programme.

Once fire barriers and insulation are complete, the team will begin **panel installation** across all four elevations.

Team Structure

- **Team 1 – Elevations D1 & D2** This team will continue installing fire barriers and insulation, preparing these elevations for the start of panel installation.
- **Team 2 – Elevations D3 & D4** This team will manage both the continuation of fire barrier and insulation works and the **striking of scaffold** on D3 and D4. Once the scaffold is removed, panel installation will be carried out using a **scissor lift**, allowing works to progress efficiently from ground level.

Additional Works

Gas Engineer Testing

Gas safety checks began on **Monday 9th March**, running alongside the ongoing façade works. Thank you to all residents who were able to accommodate their confirmed appointments — your cooperation is greatly appreciated and helps us keep the programme moving safely and efficiently.

Further gas checks are scheduled to take place on **Wednesday 18th, Thursday 19th, and Friday 20th March**. This week, you will receive a letter confirming the date and time of your **upcoming gas test appointment**. Please keep an eye out for this.

News & Updates



Our Welfare unit is located on the front entrance to the car park area between Bedford and Leicester Court



News & Updates

Due to the cut-through patch currently being closed, please follow the directions shown on the diagram to access the main road,





Contact information



Resident Liaison Officer

Name: Courtney Greatorex

Telephone: 07939 894015

Email: CGreatorex@starfishltd.com

Working hours: 8am-5:00pm



Site Manager

Name: Daniel Horwood

Telephone: 07940 022295

Email: dhorwood@starfishltd.com

Working hours: 8am-5:00pm
